

# Newington-Dover 11238M


## *October 8, 2014 Update*



Date Taken: 06/24/14- Woodbury Ave Bridge Steel Erection

# Southbound Barrel

The new northbound barrel from the existing Little Bay Bridge to Sta 1530 has been constructed. Southbound traffic is currently on this barrel as part of the traffic control plan. Exit 4 southbound traffic is temporarily using the old southbound barrel to gain access to Rt. 16. A.J. Coleman is currently constructing the new southbound barrel as well as the new Exit 4 configuration. Once the Exit 4 traffic is tied into the new southbound barrel Coleman will begin construction of the new Exit 3 southbound on and off ramps.

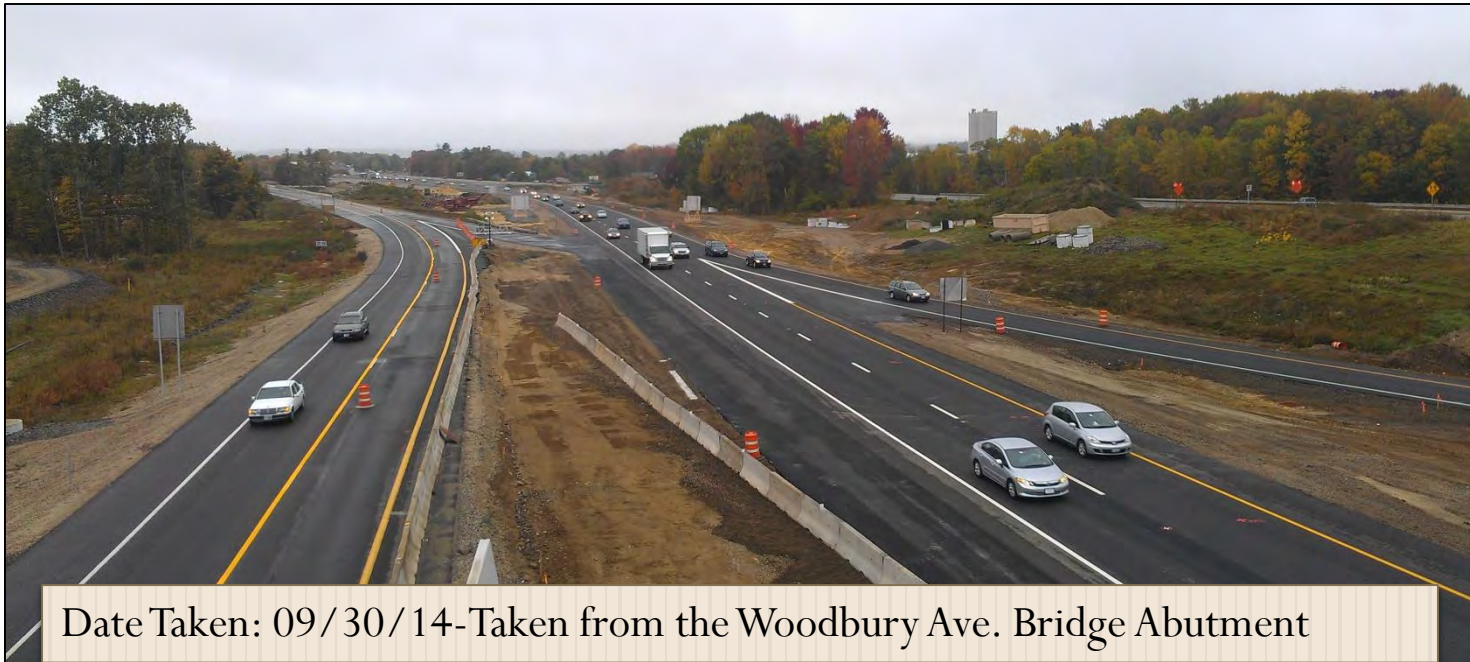

Date Taken: 09/30/14-Taken from the Woodbury Ave. Bridge Abutment

# New Exit 3

A.J. Coleman will continue construction of the new Exit 3 on and off ramp this winter. This exit will direct traffic to the Arboretum Drive and onto the new Woodbury Ave. Bridge.



Date Taken: 09/30/14- New Exit 3 on and off ramps under construction.

# Arboretum

Work on the roundabout at the intersection of Arboretum Drive, Woodbury Avenue, and the new exit 3 on /off ramp will continue into next year.



Date Taken: 09/30/14-Roundabout

# Dover

A.J. Coleman will begin construction North of the Little Bay Bridge. This work will consist of tying in the existing Rt. 16 southbound barrel to the new Little Bay Bridge approach.



Photo Date: 09/30/14- Approach to the New Little Bay Bridge.

# Shattuck Way

A.J. Coleman will continue to place selects and fine grade over the Shattuck Way Bridge. Upon completion of the Dover Rt. 16 southbound tie in, and the Shattuck way Bridge tie in, the southbound traffic will be switched onto the new Little Bay Bridge. This work is weather dependent and is scheduled to be completed December 2014.



Photo Date: 09/30/14-Shattuck Way, Newington NH

# Woodbury Ave. Bridge

E.D. SWETT has completed the bridge deck, curb, sidewalk, and island. Concrete work will finish up this year with the placement of Abutment A approach slab. The bridge will be shot blasted and membrane will be applied in the spring followed immediately by paving.



Date Taken: 08/15/14 Woodbury Bridge

# Railway Brook Restoration

The brook is approximately half way done. Coleman will continue to work as weather permits and start back up in the spring. All final plantings will be done next spring.



Date Taken: 06/18/14- Pre Construction



Date Taken: 09/29/14-Construction
